



# SKEP III Home Office Support Site Visit Report

**WAHIB  
MEDANAT**  
consultant engineers

Consultant	Wahib Medanat Consultant Engineer	Rep No.	13-08062021
Contractor	Derar Saraireh & Sons for Engineering & Contracting	Tender No.	(11/2019/USAID/SKEP/3/S) Schools for a Knowledge Economy Project (SKEP) - Phase (3) Package (1, 2)
Site Name	Khadija Bint Khwailed Basic Mixed School- Shouna Janoubia	Day/ Date	Tue. 08/06/2021
Duration of Project	450 Calendar Days	Total Project Budget	9,789,417.840 JD

No.	Visitors		Remarks
1	Suhair Amarin	- Project Dir./Head of Architectural Department	
2	Omar Elayan	-Senior Civil Engineer	
3	Akram Khammes	- Head of Electrical Department	
4	Marwan Sonna'a	-Head of Mechanical Department	
5	Hasan Shaqboua	-Quality Control Manager	

## Visit Notes

No.	Description
1	Casting for second floor slab was going on during the visit. The visitors observed the process of the casting and gave remarks to the site staff.
2	One column was defected during casting. Repair was conducted by chipping and using approved material.
3	Block work in the school has not started yet.



4	The boundary wall which shall be adjacent to neighbor should start since the Contractor received the approval before long time. Leaving the excavated area sun exposed might cause defects in the soil stability.
5	The columns at zones B and C should start.
6	Design for formwork system should be submitted by Contractor for roof slab-zone C.
7	The Contractor was informed that once the first stone layer is checked and approved, stone building can continue up to the level of window sills to avoid delay during the checking of the workshop drawings.
8	- Discussion with the Contractor as follows: <ul style="list-style-type: none"><li>• Submittals were discussed.</li><li>• The Contractor expressed his satisfaction with the Engineers' quick response regarding block work shop drawings, which accelerated works.</li><li>• Work progress as per Contractor's work schedule.</li></ul>



Project ID Sign on Site



Temperature check, sterilization and signing visitors' attendance sheet at the entrance of the site, complying with Covid-19 Protocol







One column suffered a defect during casting, Repairs were conducted by chipping and using approved material





Block work in the school has not started yet








A tour was conducted around the site



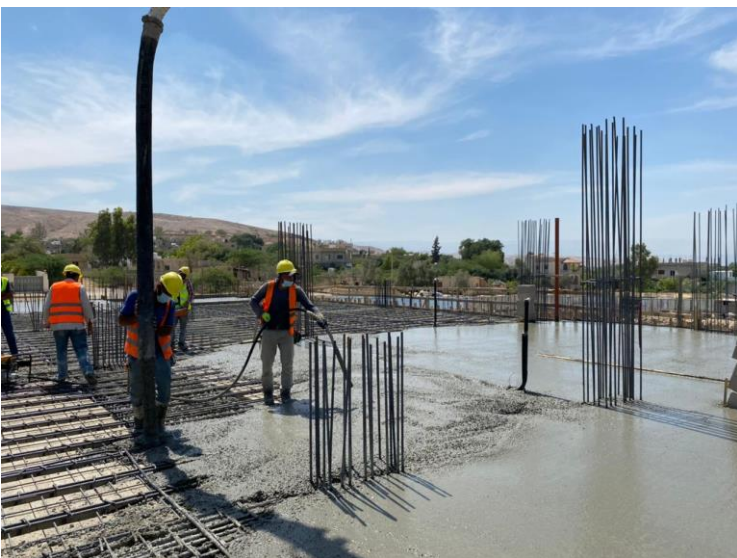

Casting for second floor slab was conducted during the visit. The visitors observed the process of the casting and gave remarks to the site staff







Discussion with the contractor as mentioned in the report



Construction of columns at zones (B) and (C) is starting



Construction of boundary wall adjacent to neighbor wall should start soon since the Contractor received approval several weeks ago
